


Northeast Interceptor (NEI) Waunakee Extension Capacity Improvements Phase 1 Project

Construction Update: 12/09/2024

BACKGROUND:

- MMSD's NEI Waunakee Extension Capacity Improvement Projects will provide additional capacity for the growing areas of Dane, Waunakee and Westport. Phase 1 provides relief and replacement sewers from the Yahara Heights County Park to the south end of the Savannah Village Subdivision.
- [Phase 1 Location and Route.](#)

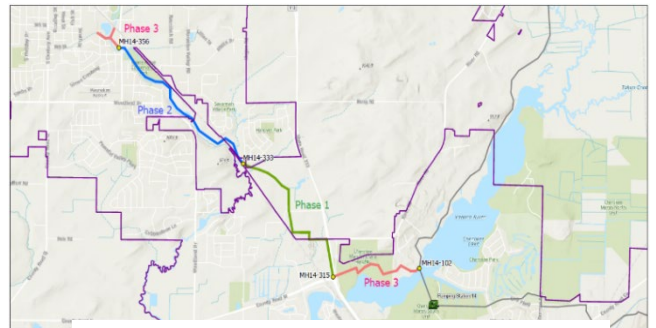

NEI – WE Capacity Improvement Overview



Setting Precast Manhole

WORK:

- [Construction Progress and Location Map](#)

- **Current Work:**

- Manhole and interceptor pipe placement along STH 113 and working north
- Dewatering, clearing and erosion control
- Pipe staging and work area set up.

- **Future Work:**

- Continue manhole and interceptor pipe placement along STH 113.
- Setup and bore steel casing and interceptor pipe under STH 113 at Kennedy Drive.
- Dewatering, erosion control, and clearing work area north of Kennedy Drive in December
- Begin manhole and pipe placement north of Kennedy Drive in January.



Setting Hobas Interceptor Pipe
W/ Dewatering (black pipe)



Installing Dewatering Ahead of Pipe Install

TRAFFIC IMPACTS:

- **STH 113:** Traffic Restrictions are currently in place:
 - o On going NB STH 113 shoulder closures
 - o Daily NB STH 113 outside lane closures from 7am to 4pm (when work requires)
- **River Road @ STH 113:**
 - o Pipe Crossing Closure –
 - *Monday, December 23rd (7am) through end of day Saturday, December 28th*
 - *Detour Route (see figure below):*
 - *STH 113 to River Rd: STH 113 to Bong Rd (east) to River Rd*
 - *River Rd to STH 113: River Rd to Bong Rd (west) to STH 113*
 - o Permanent Restoration Closure – *Summer of 2025*
- **Kennedy Drive:** – *Spring of 2025 for up to 4 months*

River Road Closure Detour Route

